

2018-19

THIRD PARTY INSPECTION REPORT

Name of the Client : **Executive Engineer,**
Electrical- Yelahanka Division,
BBMP, Bangalore.

Name of Agency : **Executive Engineer-1,**
KRIDL, Bangalore.

Name of the Work : Providing Street Lights in Ward No.08 Kodigehalli ,
BBMP, Bangalore.

Estimated Cost - Rs. 50.00 Lakhs

THIRD PARTY INSPECTION CONSULTANTS

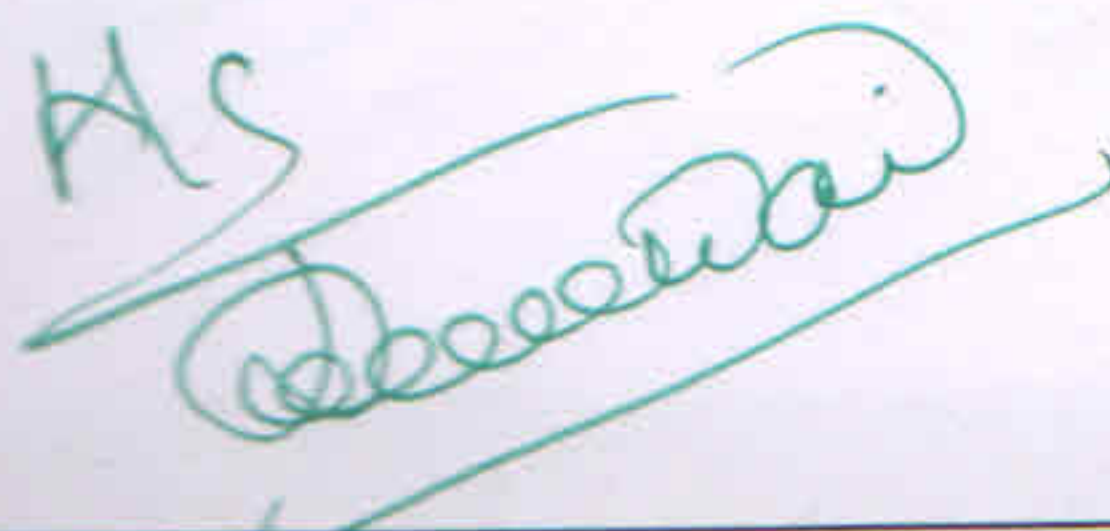
CIVIL QUALITY CONSULTANTS AND ENGINEERS

NABL Accredited as per ISO/IEC: 17025-2005 Laboratory
An ISO 9001 2008 Certified Company



#133, Bhuvaneshwarinagar, Dodda Basti Main Road, Bangalore-560056
e-mail: civilqualityconsultants@gmail.com Ph: 8553518550/9886998316

"The Road to Success is always under Construction"

HS



Executive Engineer
Electrical Division
Yelahanka Zone BBMP
Byatarayanapura, Bangalore-92



CIVIL QUALITY CONSULTANTS & ENGINEERS

(Buildings Geo-Tech & Highway Materials Testing Laboratory)

An ISO 9001: 2015 Certified Company

NABL Accredited As Per ISO/IEC : 17025:2005 Laboratory



NO: CQCE/3rd Party/Yelahanka Division/1/ 2018-19

Date: 31.10.2018

To,
Executive Engineer,
Electrical – Yelahanka Division
BBMP, Bangalore.

Sir

Sub:- Submission of 3rd Party Report for the work of Providing Street Lights in Ward No.08 Kodigehalli ,
BBMP, Bangalore.reg.

Ref:-

(i) Job code No. 008-18-000031

(ii) EE(Elec)/YZ/WO/000032/2018-19 Dated:-27/09/2018

Adverting to the above, we would like to submit the 3rd Party Inspection Report for the above said work in Electrical –Yelahanka Division along with Mr. Rajendra Nayak (Assistant Executive Engineer-1, Electrical Yelahanka Zone), and Mr. Kumar (Electrical Engineer, 3rd Party Consultants), Bangalore on 30.10.2018

The following works inspected the details of works inspected is as follows,

Sl no	Name of the work	Amount of estimate Rs in Lakhs.	Remarks
1	Providing Street Lights in Ward No.08 Kodigehalli , BBMP, Bangalore.	Rs. 50.00 Lakhs (1 st and Final bill)	Work carried out satisfactorily Details mentioned in 3 rd party compliance report

For details of works and measurements checked during the inspection time in the presence if the officials /officers afore said.

This is for favor of kind information and needful in the matter.

Enclosures: 3rd part Inspection report

Thanking you

Handwritten signature in green ink.



yours faithfully

Authorized signatory



CIVIL QUALITY CONSULTANTS & ENGINEERS

(Buildings Geo-Tech & Highway Materials Testing Laboratory)

An ISO 9001: 2015 Certified Company

NABL Accredited As Per ISO/IEC : 17025:2005 Laboratory



Name of Work : Providing Street Lights in Ward No.08 Kodigehalli , BBMP, Bangalore.

Contractor/Agency : Executive Engineer, KRIDL, Bangalore.

Name of Client : Executive Engineer, Electrical- Yelahanka Division, BBMP, Bangalore.

Total Bill Cost in Lakhs : Rs.49.9 Lakhs

Date Of Inspection : 30.10.2018

Status of Bill : First & Final Bill

In the Presence of : (a) Mr. Rajendra Nayak(Assitant Executive Engineer-1, Electrical Yelahanka Zone), BBMP, Bangalore.

: (b) Mr. kumar, (Electrical Engineer) M/s Civil Quality Consultants & Engineers, Bangalore.

3rd Party Compliance Report

Sl No	Description of the Item	Unit	Quantity	Comments / observations
1	LED Street light, Supply of LED Street light with Pressure die cast aluminum housing body with optimal heat sink for better thermal dissipation.....	Each	106	Supplied Material Quality found satisfactory
2	LED Street light, Supply of LED Street light with Pressure die cast aluminum housing body with	Each	25	Supplied Material Quality found satisfactory
3	Supplying and fixing.....mm dia class A GI pipe bracket up to 2 meters long..... Using 32mm dia G.I.Pipe	Each	123	Supplied Material Quality found satisfactory
4	Wiring for lighting/power circuit using one of PVC insulated 110V grade stranded System of wiring a)4sqmm	Each	300	Supplied Material Quality found satisfactory





CIVIL QUALITY CONSULTANTS & ENGINEERS

(Buildings Geo-Tech & Highway Materials Testing Laboratory)

An ISO 9001: 2015 Certified Company

NABL Accredited As Per ISO/IEC : 17025:2005 Laboratory



5	Fixing halogen/metal halide/SVL/IL/LED flood lights fittings over existing pole/wall ceiling including clamps bolts.....	Each	100	Supplied Material Quality found satisfactory
6	Supply erection testing & commissioning of thiristor based single/Three phase smart street light control and monitoring system remotely.....	Set	1	Supplied Material Quality found satisfactory
7	Supply and erection of single phase Thristor based smart street light control system consisting of following.....	Set	1	Supplied Material Quality found satisfactory
8	Open conduit system:Supplying heavy gauge PVC conditpipe.....dia confirming to IS 2509 with suitable size bends,junction boxes	Mtr	60	Supplied Material Quality found satisfactory
9	Supplying of 1.1KV grade Aerial bunched cable stranded&compacted Aluminum Phase Conductor.....	Mtr	100	Supplied Material Quality found satisfactory
10	Supplying and stringing of ACSR Conductor	Mtr	1000	Supplied Material Quality found satisfactory
11	Supplying and fixing....including all Hardware's etc complete as per the standard technical specification of BESCOM	Nos	29	Supplied Material Quality found satisfactory
12	No.8 Strain Insulator	Nos	10	Supplied Material Quality found satisfactory
13	Supplying and installation/ fixing/Provision of pole box with HRC fuse/MCB provision and suitable connector/terminal of 3Ph/1Ph	Each	11	Supplied Material Quality found satisfactory



Office & Laboratory : # 133, Bhuvaneshwarinagar, Dodda Basti Main Road, Bangalore - 560 056.

e-mail:civilqualityconsultants@gmail.com Ph: 080-23240644 / Mob: 8553518550



CIVIL QUALITY CONSULTANTS & ENGINEERS

(Buildings Geo-Tech & Highway Materials Testing Laboratory)

An ISO 9001: 2015 Certified Company

NABL Accredited As Per ISO/IEC : 17025:2005 Laboratory



14	Supplying and fixing moulded case circuit breaker (MCCB) over the existing wood/panel board using.....	Each	11	Supplied Material Quality found satisfactory
15	Supplying tinned copper lugs and crimping and wiring to terminal point for wire of .25sqmm long barrel	Each	70	Supplied Material Quality found satisfactory
16	Supplying of 1.1 KV LT Ug cable having aluminum conductor PVC insulated extruded.....	Nos	25	Supplied Material Quality found satisfactory
17	Wiring for lighting/power circuit using one of PVC insulated extruded inner sheathed,galvanized,steel strip....	Mtr	1400	Supplied Material Quality found satisfactory
18	Labour charges for laying of 1.1 KV class UG cable in existing trench GI pipe/stoneware.....	Mtr	1400	Supplied Material Quality found satisfactory
19	Digging of trnch of 0.6m deep x 0.50 mtr wide refilling the trench to the required ground....	Mtr	200	Supplied Material Quality found satisfactory
20	Asphalt cutting	Mtr	1000	Supplied Material Quality found satisfactory
21	Supplying and fixing 4 pole power contactor with NO/NC contacts on existing wood/panel....	Nos	2	Supplied Material Quality found satisfactory
22	Supply and fixing miniature circuit breakers on existing MCB distribution boards.....	Nos	2	Supplied Material Quality found satisfactory
23	Supply and fixing of twin dial electro mechanical timer(without contactor)using ...	Nos	2	Supplied Material Quality found satisfactory





CIVIL QUALITY CONSULTANTS & ENGINEERS

(Buildings Geo-Tech & Highway Materials Testing Laboratory)

An ISO 9001: 2015 Certified Company

NABL Accredited As Per ISO/IEC : 17025:2005 Laboratory



24	Wiring for lighting/power circuit using one FRLS PVC insulated 1100V grade multistrand copper conductor single core wire in open or concealed	Mtr	300	Supplied Material Quality found satisfactory
25	6 sqmm	Mtr	10	Supplied Material Quality found satisfactory

Verified By



For CIVIL QUALITY CONSULTANTS & ENGINEERS
Authorised Signatory

Authorised Signatory

Providing Street Lights in Ward No.08 Kodigehalli , BBMP, Bangalore.



Providing Street Lights in Ward No.08 Kodigehalli , BBMP, Bangalore.

